


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 04.03.2021
89312 Günzburg-Deffingen	Koordinaten: 32531451.06 / 5679116.28	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	1
0.20	1
0.30	1
0.40	1
0.50	1
0.60	1
0.70	2
0.80	1
0.90	1
1.00	2
1.10	2
1.20	3
1.30	5
1.40	4
1.50	3
1.60	2
1.70	4
1.80	7
1.90	6
2.00	5
2.10	5
2.20	5
2.30	4
2.40	4
2.50	2
2.60	2
2.70	3
2.80	2
2.90	3
3.00	3
3.10	3
3.20	2
3.30	2
3.40	2
3.50	3
3.60	5
3.70	4
3.80	5
3.90	5
4.00	6
4.10	6
4.20	5
4.30	6
4.40	6
4.50	5
4.60	7
4.70	7
4.80	8
4.90	9
5.00	10
5.10	11
5.20	11
5.30	12
5.40	11
5.50	12
5.60	11
5.70	12
5.80	11
5.90	11
6.00	11

DPH 1/20


Ansatzpunkt: 201.55 m NHN

DPH Anzahl Schläge N10H

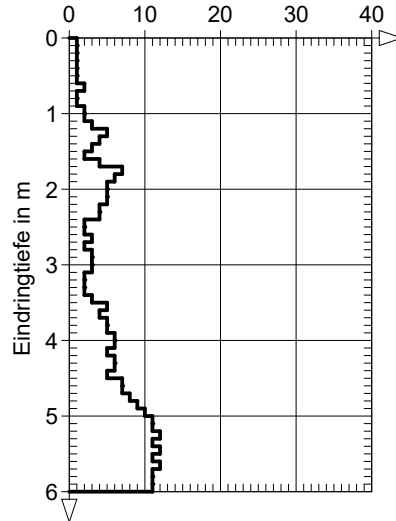


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 04.03.2021
89312 Günzburg-Deffingen	Koordinaten: 32531686.14 / 5679101.07	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	1
0.20	1
0.30	1
0.40	1
0.50	1
0.60	1
0.70	1
0.80	1
0.90	1
1.00	5
1.10	7
1.20	6
1.30	5
1.40	3
1.50	3
1.60	2
1.70	8
1.80	4
1.90	5
2.00	4
2.10	5
2.20	7
2.30	6
2.40	4
2.50	4
2.60	3
2.70	4
2.80	3
2.90	3
3.00	3
3.10	3
3.20	3
3.30	3
3.40	2
3.50	3
3.60	4
3.70	4
3.80	5
3.90	5
4.00	5
4.10	4
4.20	3
4.30	3
4.40	4
4.50	3
4.60	4
4.70	3
4.80	3
4.90	4
5.00	3
5.10	4
5.20	3
5.30	4
5.40	4
5.50	4
5.60	4
5.70	4
5.80	4
5.90	4
6.00	4

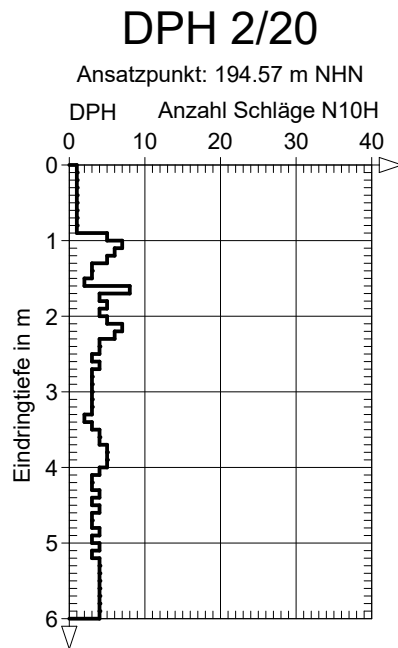


Terrasond GmbH & Co.KG		Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16		Projektnr.: 2020-1029	Datum: 28.10.2020
89312 Günzburg-Deffingen		Koordinaten: 32531887.65 / 5679077.42	
Tel.: 08221/906-0/ Fax: -40		Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀	Tiefe	N ₁₀
0.10	12	6.10	9
0.20	11	6.20	9
0.30	12	6.30	9
0.40	15	6.40	9
0.50	15	6.50	9
0.60	15	6.60	8
0.70	14	6.70	7
0.80	15	6.80	6
0.90	7	6.90	6
1.00	7	7.00	7
1.10	10	7.10	6
1.20	9	7.20	5
1.30	10	7.30	5
1.40	9	7.40	4
1.50	8	7.50	4
1.60	9	7.60	4
1.70	8	7.70	4
1.80	9	7.80	5
1.90	10	7.90	4
2.00	9	8.00	5
2.10	10		
2.20	11		
2.30	10		
2.40	10		
2.50	9		
2.60	8		
2.70	8		
2.80	8		
2.90	7		
3.00	8		
3.10	9		
3.20	10		
3.30	9		
3.40	9		
3.50	8		
3.60	8		
3.70	9		
3.80	8		
3.90	9		
4.00	9		
4.10	9		
4.20	10		
4.30	9		
4.40	10		
4.50	10		
4.60	11		
4.70	11		
4.80	11		
4.90	10		
5.00	8		
5.10	9		
5.20	8		
5.30	9		
5.40	9		
5.50	9		
5.60	10		
5.70	11		
5.80	11		
5.90	11		
6.00	11		

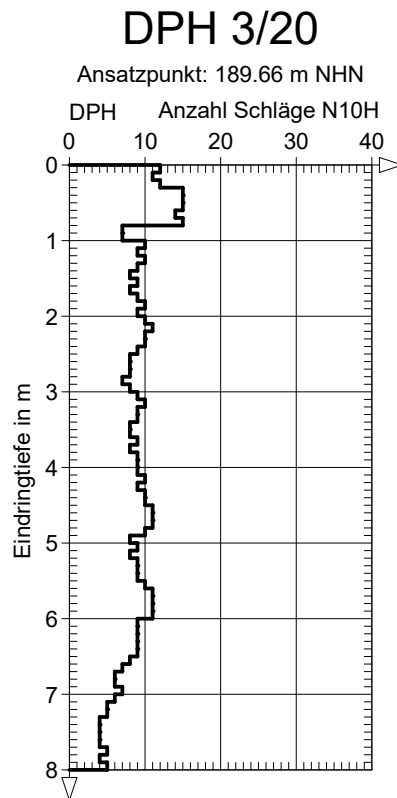


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 21.10.2020
89312 Günzburg-Deffingen	Koordinaten: 32532140.36 / 5679079.33	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀	Tiefe	N ₁₀
0.10	0	6.10	9
0.20	0	6.20	10
0.30	8	6.30	11
0.40	10	6.40	10
0.50	6	6.50	10
0.60	5	6.60	10
0.70	1	6.70	10
0.80	1	6.80	9
0.90	2	6.90	10
1.00	1	7.00	11
1.10	1	7.10	13
1.20	1	7.20	13
1.30	1	7.30	15
1.40	1	7.40	14
1.50	1	7.50	15
1.60	1	7.60	15
1.70	2	7.70	15
1.80	2	7.80	16
1.90	2	7.90	20
2.00	2	8.00	19
2.10	2		
2.20	3		
2.30	5		
2.40	6		
2.50	5		
2.60	4		
2.70	5		
2.80	13		
2.90	19		
3.00	21		
3.10	17		
3.20	11		
3.30	9		
3.40	10		
3.50	10		
3.60	8		
3.70	9		
3.80	8		
3.90	7		
4.00	5		
4.10	3		
4.20	3		
4.30	4		
4.40	3		
4.50	3		
4.60	4		
4.70	4		
4.80	6		
4.90	7		
5.00	11		
5.10	12		
5.20	10		
5.30	11		
5.40	11		
5.50	11		
5.60	13		
5.70	16		
5.80	21		
5.90	13		
6.00	11		

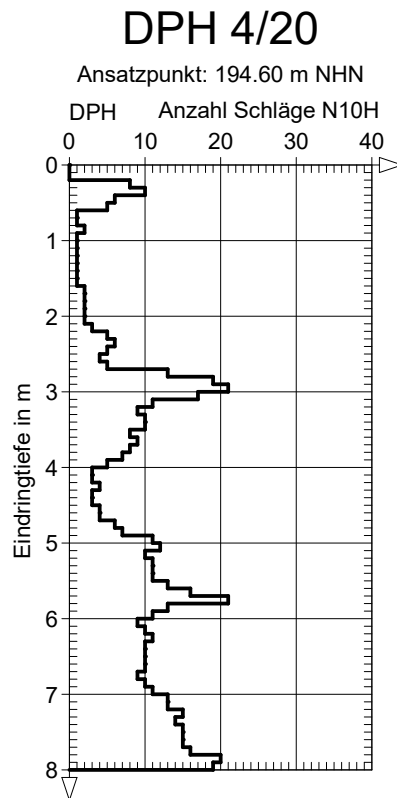


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 21.10.2020
89312 Günzburg-Deffingen	Koordinaten: 32532201.24 / 5679028.59	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	3
0.20	7
0.30	6
0.40	7
0.50	7
0.60	2
0.70	0
0.80	0
0.90	1
1.00	2
1.10	3
1.20	4
1.30	3
1.40	3
1.50	2
1.60	3
1.70	2
1.80	4
1.90	4
2.00	4
2.10	4
2.20	3
2.30	4
2.40	4
2.50	6
2.60	5
2.70	5
2.80	5
2.90	4
3.00	7
3.10	7
3.20	9
3.30	9
3.40	10
3.50	11
3.60	8
3.70	8
3.80	7
3.90	6
4.00	6
4.10	7
4.20	8
4.30	13
4.40	27
4.50	22
4.60	20
4.70	22
4.80	26
4.90	25
5.00	21
5.10	19
5.20	15
5.30	14
5.40	14
5.50	16
5.60	15
5.70	9
5.80	7
5.90	7
6.00	7

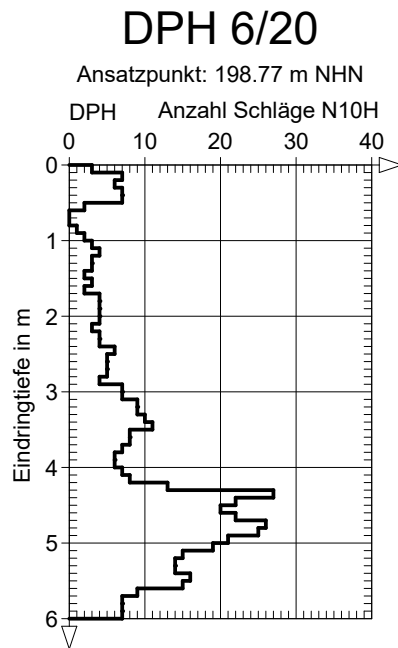


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke		
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 14.10.2020	
89312 Günzburg-Deffingen	Koordinaten: 32532341.75 / 5679037.72		
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann	

Tiefe	N ₁₀	Tiefe	N ₁₀
0.10	0	6.10	5
0.20	3	6.20	3
0.30	2	6.30	4
0.40	5	6.40	4
0.50	12	6.50	5
0.60	12	6.60	5
0.70	13	6.70	5
0.80	12	6.80	5
0.90	7	6.90	7
1.00	7	7.00	7
1.10	3	7.10	9
1.20	3	7.20	9
1.30	3	7.30	10
1.40	3	7.40	13
1.50	3	7.50	11
1.60	3	7.60	14
1.70	9	7.70	15
1.80	1	7.80	16
1.90	1		
2.00	1		
2.10	2		
2.20	1		
2.30	2		
2.40	4		
2.50	4		
2.60	5		
2.70	2		
2.80	2		
2.90	2		
3.00	4		
3.10	1		
3.20	1		
3.30	1		
3.40	2		
3.50	1		
3.60	3		
3.70	3		
3.80	4		
3.90	4		
4.00	4		
4.10	6		
4.20	5		
4.30	5		
4.40	7		
4.50	9		
4.60	9		
4.70	7		
4.80	7		
4.90	6		
5.00	5		
5.10	4		
5.20	4		
5.30	6		
5.40	8		
5.50	10		
5.60	12		
5.70	13		
5.80	15		
5.90	12		
6.00	10		

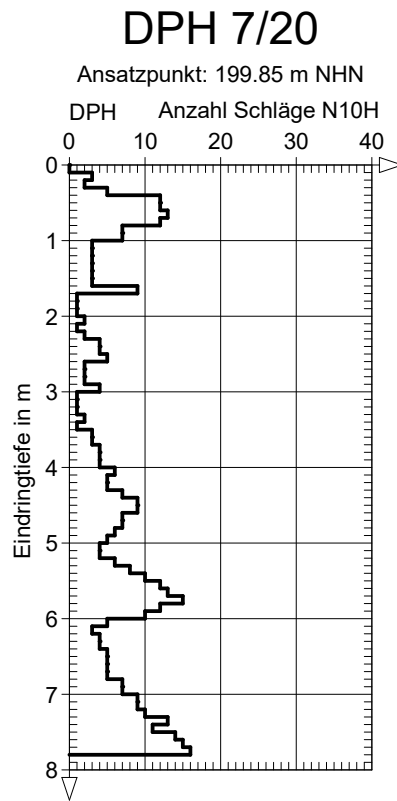

Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke		
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 28.10.2020	
89312 Günzburg-Deffingen	Koordinaten: 32532757.80 / 5679019.58		
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann	

Tiefe	N ₁₀	Tiefe	N ₁₀
0.10	1	6.10	7
0.20	4	6.20	9
0.30	5	6.30	10
0.40	5	6.40	11
0.50	3	6.50	13
0.60	3	6.60	14
0.70	4	6.70	14
0.80	4	6.80	15
0.90	3	6.90	15
1.00	3	7.00	16
1.10	2	7.10	17
1.20	2	7.20	17
1.30	2	7.30	17
1.40	2	7.40	15
1.50	1	7.50	18
1.60	1	7.60	17
1.70	1	7.70	18
1.80	1	7.80	18
1.90	1	7.90	18
2.00	1	8.00	18
2.10	2		
2.20	2		
2.30	2		
2.40	2		
2.50	2		
2.60	3		
2.70	2		
2.80	3		
2.90	4		
3.00	4		
3.10	4		
3.20	4		
3.30	6		
3.40	5		
3.50	5		
3.60	5		
3.70	5		
3.80	5		
3.90	5		
4.00	5		
4.10	5		
4.20	4		
4.30	5		
4.40	5		
4.50	4		
4.60	5		
4.70	5		
4.80	5		
4.90	5		
5.00	6		
5.10	6		
5.20	8		
5.30	7		
5.40	8		
5.50	7		
5.60	7		
5.70	8		
5.80	7		
5.90	7		
6.00	7		

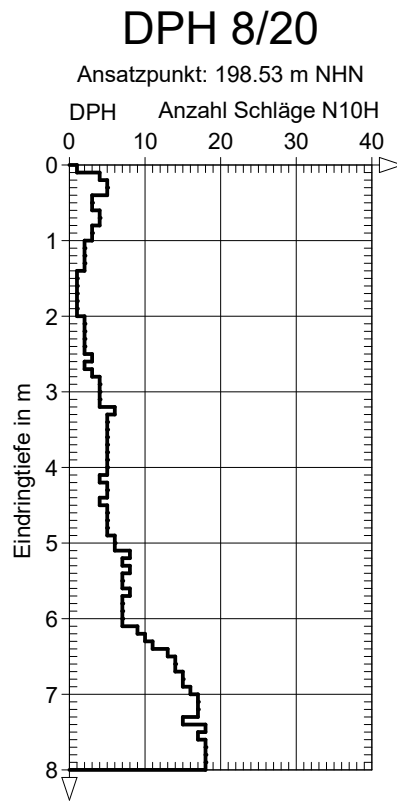


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke		
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 29.10.2020	
89312 Günzburg-Deffingen	Koordinaten: 32533036.15 / 5678934.26		
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann	

Tiefe	N ₁₀	Tiefe	N ₁₀
0.10	3	6.10	2
0.20	6	6.20	2
0.30	10	6.30	2
0.40	11	6.40	3
0.50	13	6.50	3
0.60	12	6.60	3
0.70	13	6.70	3
0.80	19	6.80	4
0.90	15	6.90	3
1.00	9	7.00	4
1.10	5	7.10	5
1.20	8	7.20	5
1.30	4	7.30	7
1.40	3	7.40	28
1.50	3	7.50	15
1.60	5	7.60	12
1.70	4	7.70	11
1.80	4	7.80	7
1.90	3	7.90	19
2.00	3	8.00	30
2.10	4	8.10	41
2.20	4	8.20	31
2.30	3	8.30	14
2.40	2	8.40	10
2.50	2	8.50	13
2.60	2	8.60	18
2.70	3	8.70	40
2.80	3	8.80	100
2.90	2	8.90	115
3.00	4		
3.10	3		
3.20	3		
3.30	3		
3.40	4		
3.50	3		
3.60	4		
3.70	4		
3.80	4		
3.90	3		
4.00	4		
4.10	4		
4.20	3		
4.30	2		
4.40	2		
4.50	2		
4.60	2		
4.70	2		
4.80	4		
4.90	4		
5.00	3		
5.10	4		
5.20	2		
5.30	2		
5.40	3		
5.50	3		
5.60	3		
5.70	2		
5.80	2		
5.90	2		
6.00	2		


DPH 9A/20

Ansatzpunkt: 189.75 m NHN

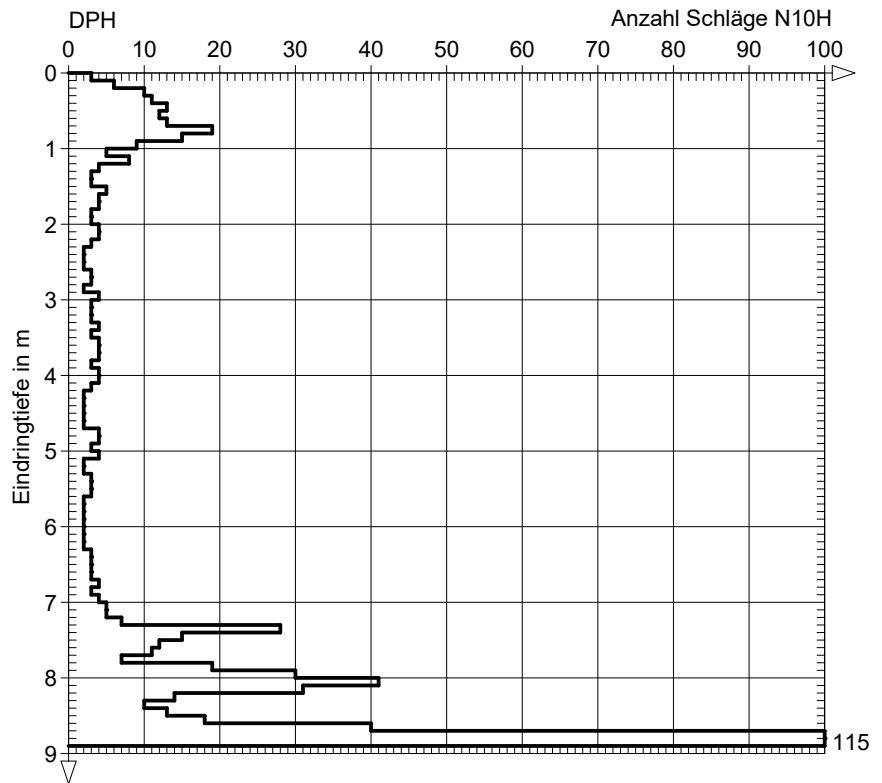


Terrasond GmbH & Co.KG		Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16		Projektnr.: 2020-1029	Datum: 15.10.2020
89312 Günzburg-Deffingen		Koordinaten: 32533293.86 / 5678947.31	
Tel.: 08221/906-0/ Fax: -40		Maßstab: 1: 100	Ausgeführt von: Andreas Schaepmann

Tiefe	N ₁₀
0.10	0
0.20	4
0.30	19
0.40	36
0.50	16
0.60	17
0.70	18
0.80	22
0.90	22
1.00	21
1.10	22
1.20	9
1.30	6
1.40	9
1.50	11
1.60	10
1.70	8
1.80	8
1.90	10
2.00	11
2.10	10
2.20	11
2.30	12
2.40	13
2.50	13
2.60	12
2.70	9
2.80	10
2.90	9
3.00	8
3.10	8
3.20	9
3.30	10
3.40	12
3.50	12
3.60	11
3.70	11
3.80	10
3.90	13
4.00	15
4.10	18
4.20	23
4.30	33
4.40	28
4.50	24
4.60	26
4.70	24
4.80	31
4.90	85

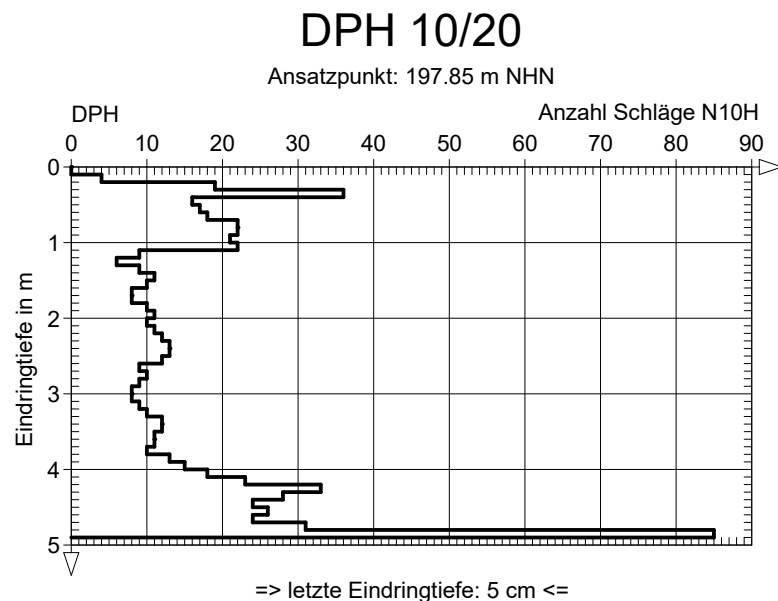


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 22.10.2020
89312 Günzburg-Deffingen	Koordinaten: 32533424.96 / 5678970.42	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	9
0.20	13
0.30	12
0.40	8
0.50	10
0.60	30
0.70	30
0.80	20
0.90	14
1.00	7
1.10	5
1.20	4
1.30	7
1.40	8
1.50	7
1.60	6
1.70	7
1.80	9
1.90	3
2.00	6
2.10	9
2.20	12
2.30	6
2.40	3
2.50	4
2.60	5
2.70	5
2.80	4
2.90	9
3.00	16
3.10	15
3.20	10
3.30	7
3.40	9
3.50	13
3.60	15
3.70	16
3.80	13
3.90	16
4.00	15
4.10	11
4.20	20
4.30	24
4.40	20
4.50	16
4.60	16
4.70	10
4.80	6
4.90	7
5.00	10
5.10	8
5.20	8
5.30	6
5.40	12
5.50	12
5.60	8
5.70	7
5.80	5
5.90	8
6.00	12

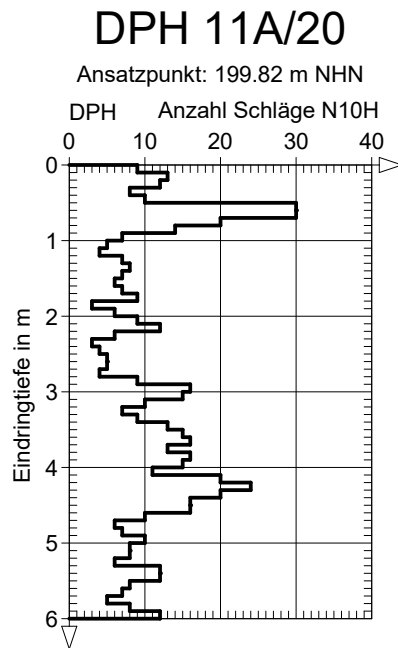


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke		
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 15.10.2020	
89312 Günzburg-Deffingen	Koordinaten: 32533418.90 / 5678926.62		
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann	

Tiefe	N ₁₀	Tiefe	N ₁₀
0.10	0	6.10	14
0.20	4	6.20	9
0.30	4	6.30	10
0.40	4	6.40	11
0.50	6	6.50	8
0.60	9	6.60	11
0.70	19	6.70	18
0.80	25	6.80	13
0.90	24	6.90	17
1.00	14	7.00	15
1.10	8	7.10	15
1.20	4	7.20	11
1.30	4	7.30	11
1.40	5	7.40	17
1.50	13	7.50	18
1.60	12	7.60	16
1.70	8	7.70	24
1.80	8	7.80	24
1.90	11	7.90	20
2.00	7	8.00	20
2.10	10	8.10	18
2.20	17	8.20	17
2.30	13	8.30	15
2.40	19	8.40	15
2.50	19	8.50	11
2.60	10	8.60	11
2.70	6	8.70	12
2.80	7	8.80	14
2.90	8	8.90	16
3.00	9		
3.10	7		
3.20	8		
3.30	7		
3.40	7		
3.50	12		
3.60	8		
3.70	5		
3.80	3		
3.90	4		
4.00	6		
4.10	12		
4.20	14		
4.30	9		
4.40	7		
4.50	7		
4.60	4		
4.70	4		
4.80	7		
4.90	4		
5.00	4		
5.10	6		
5.20	6		
5.30	10		
5.40	12		
5.50	10		
5.60	12		
5.70	13		
5.80	14		
5.90	12		
6.00	13		

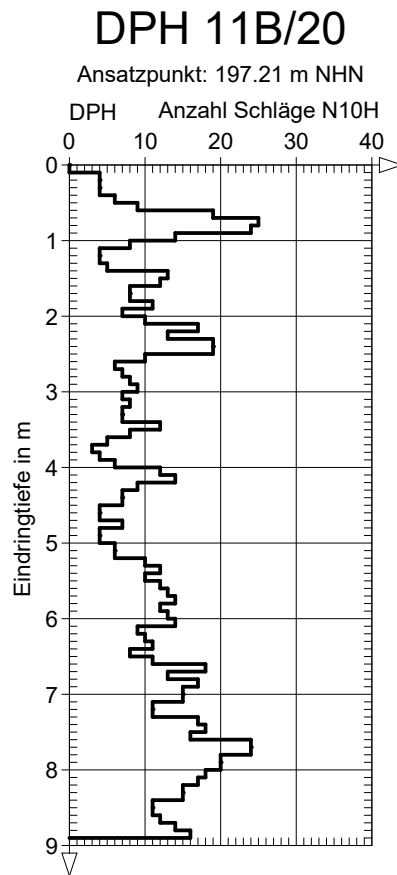


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 22.10.2020
89312 Günzburg-Deffingen	Koordinaten: 32533534.89 / 5678932.48	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	3
0.20	5
0.30	9
0.40	9
0.50	8
0.60	8
0.70	10
0.80	13
0.90	13
1.00	15
1.10	17
1.20	11
1.30	10
1.40	10
1.50	9
1.60	8
1.70	5
1.80	5
1.90	6
2.00	6
2.10	4
2.20	3
2.30	4
2.40	6
2.50	7
2.60	5
2.70	5
2.80	8
2.90	8
3.00	6
3.10	6
3.20	8
3.30	10
3.40	8
3.50	10
3.60	13
3.70	9
3.80	7
3.90	10
4.00	7
4.10	10
4.20	12
4.30	13
4.40	13
4.50	13
4.60	9
4.70	5
4.80	5
4.90	7
5.00	9
5.10	8
5.20	6
5.30	7
5.40	9
5.50	8
5.60	6
5.70	6
5.80	6
5.90	5
6.00	5

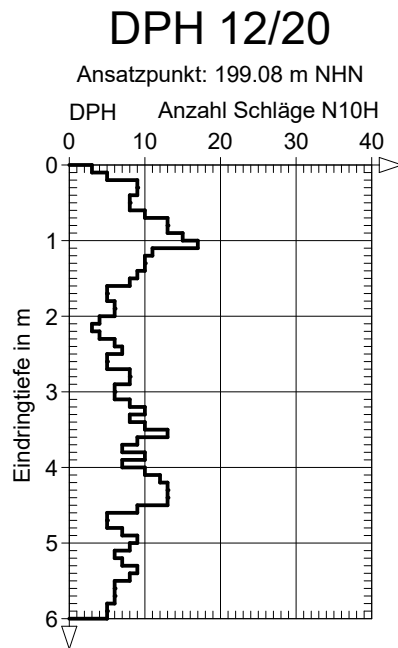

Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 22.10.2020
89312 Günzburg-Deffingen	Koordinaten: 32533649.59 / 5678947.65	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaepmann

Tiefe	N ₁₀
0.10	3
0.20	8
0.30	11
0.40	13
0.50	8
0.60	14
0.70	22
0.80	32
0.90	31
1.00	37
1.10	48
1.20	150

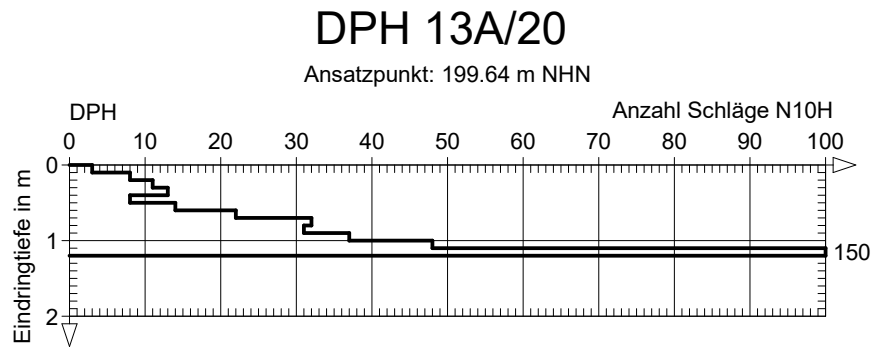


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 23.10.2020
89312 Günzburg-Deffingen	Koordinaten: 32533633.01 / 5678906.13	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaepmann

Tiefe	N ₁₀
0.10	2
0.20	4
0.30	9
0.40	8
0.50	9
0.60	14
0.70	14
0.80	14
0.90	12
1.00	9
1.10	8
1.20	10
1.30	10
1.40	8
1.50	8
1.60	7
1.70	9
1.80	10
1.90	8
2.00	8
2.10	10
2.20	10
2.30	10
2.40	10
2.50	10
2.60	10
2.70	9
2.80	9
2.90	10
3.00	9
3.10	17
3.20	17
3.30	6
3.40	6
3.50	7
3.60	14
3.70	9
3.80	10
3.90	5
4.00	29
4.10	20
4.20	27
4.30	25
4.40	14
4.50	7
4.60	6
4.70	5
4.80	5
4.90	5
5.00	3
5.10	3
5.20	4
5.30	14
5.40	8
5.50	22
5.60	160


DPH 13B/20

Ansatzpunkt: 199.63 m NHN

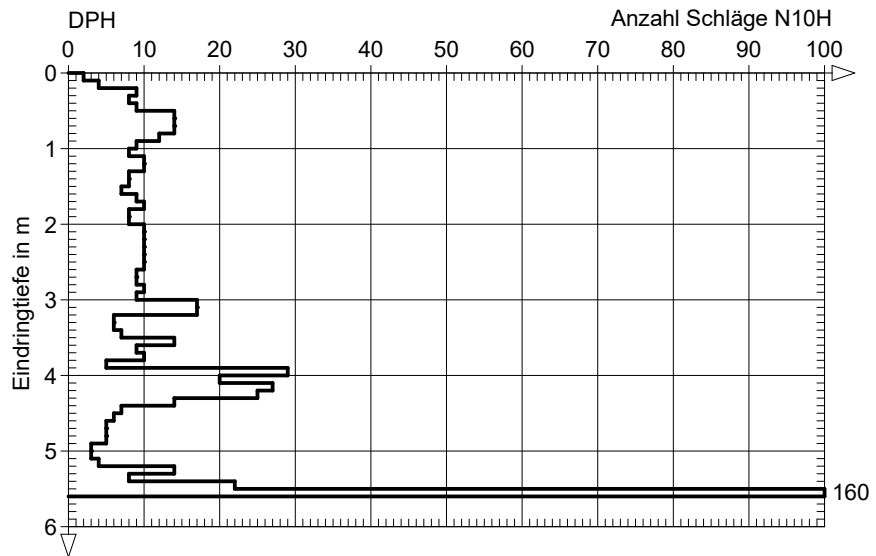


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 08.12.2020
89312 Günzburg-Deffingen	Koordinaten: 32533732.13 / 5678917.67	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	2
0.20	2
0.30	2
0.40	2
0.50	9
0.60	20
0.70	25
0.80	23
0.90	25
1.00	20
1.10	18
1.20	15
1.30	10
1.40	9
1.50	13
1.60	14
1.70	13
1.80	9
1.90	9
2.00	7
2.10	8
2.20	10
2.30	10
2.40	7
2.50	10
2.60	13
2.70	20
2.80	21
2.90	19
3.00	24
3.10	25
3.20	24
3.30	22
3.40	21
3.50	22
3.60	19
3.70	14
3.80	13
3.90	9
4.00	10
4.10	8
4.20	7
4.30	8
4.40	13
4.50	11
4.60	10
4.70	9
4.80	13
4.90	16
5.00	19
5.10	19
5.20	16
5.30	13
5.40	13
5.50	13
5.60	12
5.70	15
5.80	88
5.90	100

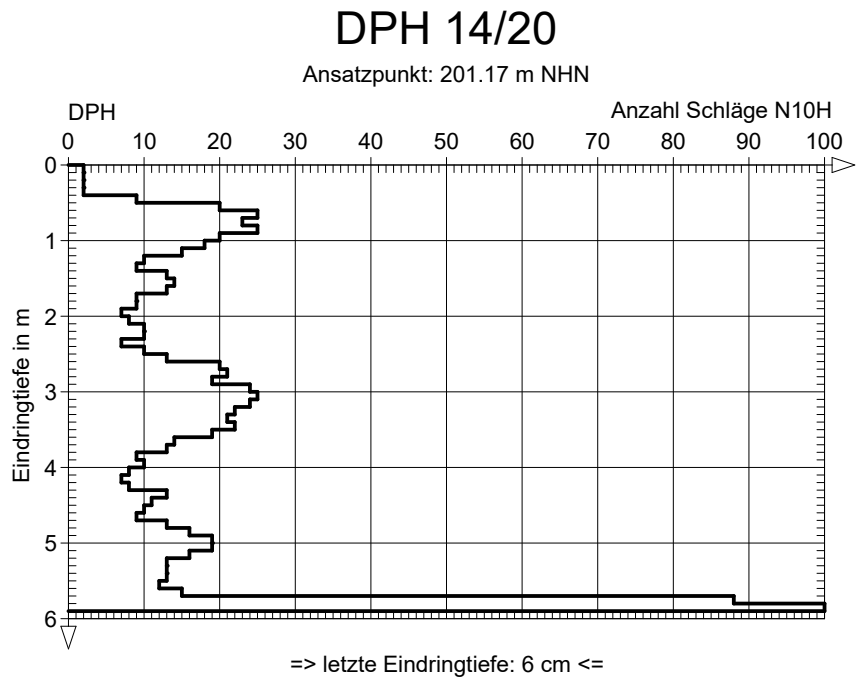

Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke		
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 04.03.2021	
89312 Günzburg-Deffingen	Koordinaten: 32534056.59 / 5678826.70		
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann	

Tiefe	N ₁₀	Tiefe	N ₁₀
0.10	3	6.10	8
0.20	4	6.20	5
0.30	5	6.30	5
0.40	5	6.40	24
0.50	7	6.50	50
0.60	9		
0.70	9		
0.80	7		
0.90	6		
1.00	8		
1.10	11		
1.20	14		
1.30	17		
1.40	22		
1.50	24		
1.60	19		
1.70	14		
1.80	17		
1.90	19		
2.00	19		
2.10	19		
2.20	18		
2.30	21		
2.40	30		
2.50	20		
2.60	18		
2.70	13		
2.80	9		
2.90	7		
3.00	13		
3.10	13		
3.20	11		
3.30	10		
3.40	8		
3.50	13		
3.60	16		
3.70	17		
3.80	17		
3.90	14		
4.00	14		
4.10	12		
4.20	12		
4.30	11		
4.40	10		
4.50	13		
4.60	10		
4.70	11		
4.80	10		
4.90	9		
5.00	7		
5.10	6		
5.20	8		
5.30	10		
5.40	10		
5.50	10		
5.60	10		
5.70	9		
5.80	7		
5.90	8		
6.00	8		

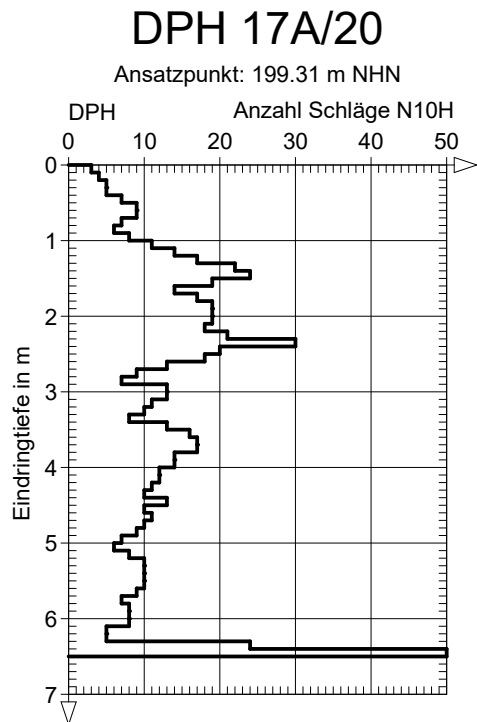


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 27.10.2020
89312 Günzburg-Deffingen	Koordinaten: 32534087.16 / 5678748.99	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	6
0.20	15
0.30	13
0.40	7
0.50	3
0.60	1
0.70	2
0.80	3
0.90	3
1.00	4
1.10	3
1.20	2
1.30	3
1.40	3
1.50	4
1.60	4
1.70	5
1.80	4
1.90	3
2.00	4
2.10	4
2.20	6
2.30	7
2.40	14
2.50	10
2.60	8
2.70	11
2.80	11
2.90	10
3.00	11
3.10	16
3.20	14
3.30	13
3.40	11
3.50	10
3.60	11
3.70	14
3.80	14
3.90	12
4.00	10
4.10	10
4.20	9
4.30	7
4.40	6
4.50	5
4.60	4
4.70	5
4.80	5
4.90	6
5.00	6
5.10	6
5.20	5
5.30	7
5.40	24
5.50	54
5.60	80
5.70	115


DPH 18/20

Ansatzpunkt: 198.48 m NHN

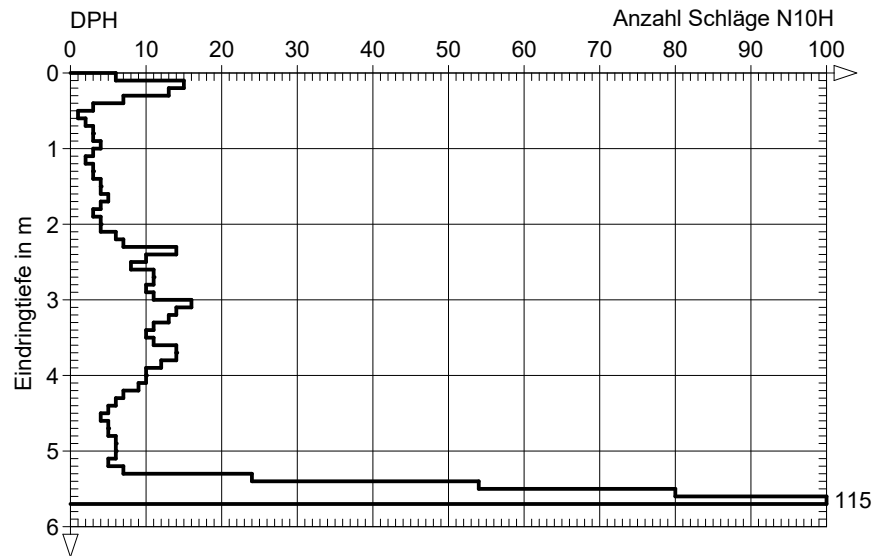


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 26.01.2021
89312 Günzburg-Deffingen	Koordinaten: 32535539.50 / 5678265.58	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	1
0.20	2
0.30	4
0.40	3
0.50	1
0.60	2
0.70	2
0.80	2
0.90	3
1.00	3
1.10	3
1.20	2
1.30	2
1.40	2
1.50	2
1.60	2
1.70	2
1.80	3
1.90	2
2.00	2
2.10	2
2.20	2
2.30	2
2.40	1
2.50	2
2.60	2
2.70	3
2.80	4
2.90	3
3.00	3
3.10	3
3.20	3
3.30	2
3.40	4
3.50	17
3.60	21
3.70	26
3.80	24
3.90	13
4.00	6
4.10	4
4.20	4
4.30	3
4.40	4
4.50	5
4.60	7
4.70	16
4.80	11
4.90	13
5.00	18

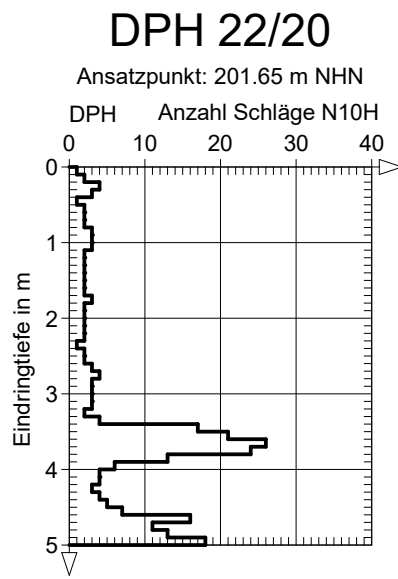

Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 26.01.2021
89312 Günzburg-Deffingen	Koordinaten: 32535553.04 / 5678197.39	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	2
0.20	2
0.30	3
0.40	4
0.50	2
0.60	1
0.70	1
0.80	1
0.90	1
1.00	1
1.10	1
1.20	1
1.30	1
1.40	1
1.50	1
1.60	1
1.70	1
1.80	1
1.90	1
2.00	1
2.10	3
2.20	3
2.30	2
2.40	3
2.50	3
2.60	3
2.70	3
2.80	3
2.90	4
3.00	4
3.10	3
3.20	4
3.30	3
3.40	4
3.50	5
3.60	4
3.70	5
3.80	4
3.90	4
4.00	5
4.10	5
4.20	6
4.30	6
4.40	6
4.50	7
4.60	8
4.70	8
4.80	6
4.90	6
5.00	6
5.10	6
5.20	7
5.30	8
5.40	8
5.50	8
5.60	17
5.70	17
5.80	12
5.90	11
6.00	9

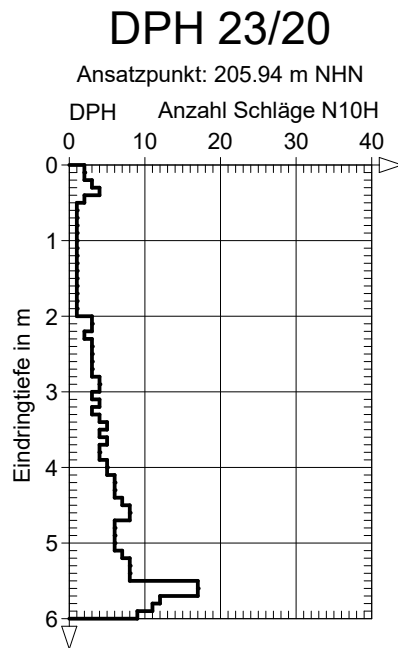


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke		
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 26.01.2021	
89312 Günzburg-Deffingen	Koordinaten: 32535592.33 / 5678241.69		
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann	

Tiefe	N ₁₀	Tiefe	N ₁₀
0.10	1	6.10	6
0.20	2	6.20	6
0.30	2	6.30	7
0.40	3	6.40	7
0.50	5	6.50	7
0.60	5	6.60	8
0.70	5	6.70	8
0.80	5	6.80	8
0.90	5	6.90	8
1.00	5	7.00	16
1.10	3	7.10	17
1.20	4	7.20	14
1.30	5	7.30	32
1.40	5	7.40	26
1.50	4	7.50	12
1.60	4	7.60	100
1.70	4		
1.80	4		
1.90	5		
2.00	5		
2.10	3		
2.20	3		
2.30	3		
2.40	2		
2.50	3		
2.60	4		
2.70	4		
2.80	4		
2.90	5		
3.00	3		
3.10	3		
3.20	2		
3.30	3		
3.40	3		
3.50	6		
3.60	7		
3.70	6		
3.80	8		
3.90	7		
4.00	7		
4.10	7		
4.20	7		
4.30	4		
4.40	6		
4.50	5		
4.60	4		
4.70	3		
4.80	4		
4.90	5		
5.00	4		
5.10	5		
5.20	5		
5.30	5		
5.40	5		
5.50	5		
5.60	5		
5.70	6		
5.80	5		
5.90	5		
6.00	6		

DPH 24/20


Ansatzpunkt: 206.36 m NHN

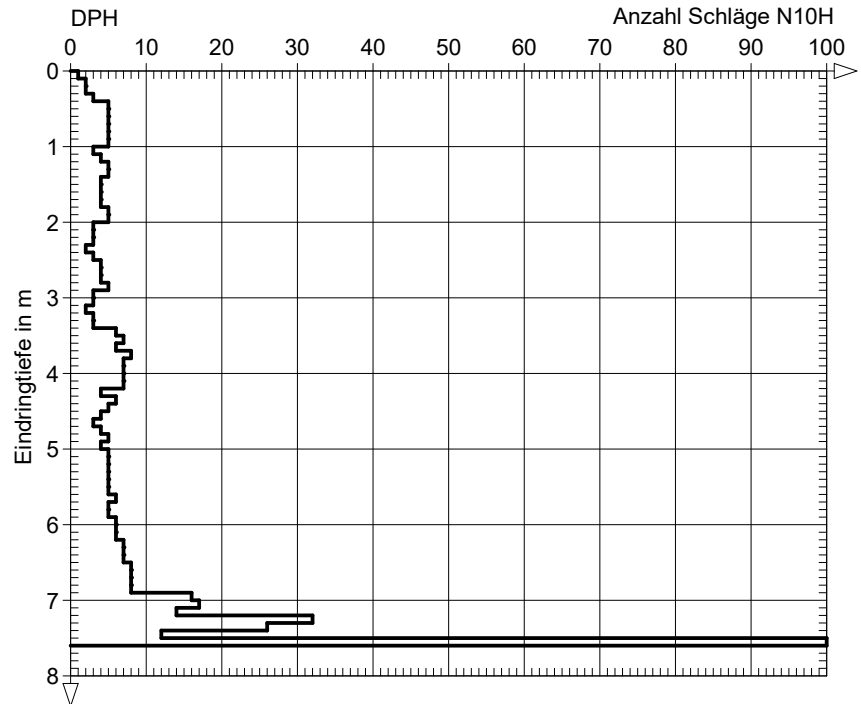

=> letzte Eindringtiefe: 7,65 m <=


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 19.04.2021
89312 Günzburg-Deffingen	Koordinaten: 32535983.66 / 5678300.00	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	1
0.20	2
0.30	2
0.40	2
0.50	2
0.60	1
0.70	1
0.80	2
0.90	2
1.00	1
1.10	2
1.20	2
1.30	1
1.40	1
1.50	1
1.60	1
1.70	18
1.80	16
1.90	5
2.00	5
2.10	4
2.20	6
2.30	6
2.40	6
2.50	16
2.60	52
2.70	23
2.80	10
2.90	7
3.00	8
3.10	7
3.20	8
3.30	7
3.40	8
3.50	9
3.60	12
3.70	12
3.80	12
3.90	11
4.00	10
4.10	11
4.20	12
4.30	13
4.40	17
4.50	13
4.60	12
4.70	17
4.80	17
4.90	15
5.00	13
5.10	12
5.20	13
5.30	12
5.40	15
5.50	16

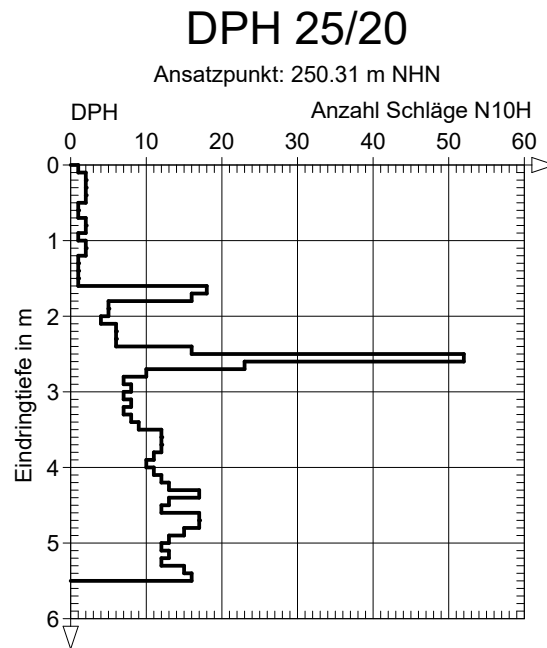


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projekttr.: 2020-1029	Datum: 21.01.2021
89312 Günzburg-Deffingen	Koordinaten: 32536262.46 / 5678261.61	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	2
0.20	3
0.30	4
0.40	2
0.50	2
0.60	3
0.70	2
0.80	3
0.90	3
1.00	4
1.10	4
1.20	6
1.30	6
1.40	7
1.50	7
1.60	8
1.70	18
1.80	11
1.90	7
2.00	16
2.10	12
2.20	5
2.30	5
2.40	6
2.50	6
2.60	6
2.70	6
2.80	5
2.90	9
3.00	8
3.10	29
3.20	10
3.30	6
3.40	9
3.50	6
3.60	8
3.70	6
3.80	4
3.90	4
4.00	4
4.10	4
4.20	5
4.30	6
4.40	7
4.50	9
4.60	6
4.70	7
4.80	8
4.90	8
5.00	10

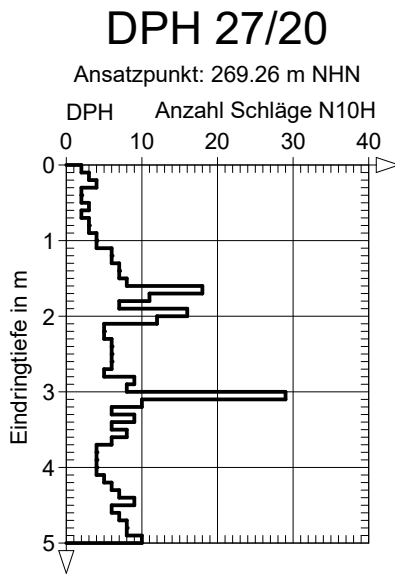


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 21.01.2021
89312 Günzburg-Deffingen	Koordinaten: 32536264.36 / 5678449.34	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaepmann

Tiefe	N ₁₀
0.10	2
0.20	3
0.30	8
0.40	5
0.50	7
0.60	3
0.70	3
0.80	8
0.90	13
1.00	15
1.10	15
1.20	15
1.30	13
1.40	22
1.50	23
1.60	21
1.70	22
1.80	34
1.90	19
2.00	17
2.10	25
2.20	26
2.30	34
2.40	66
2.50	22
2.60	54
2.70	79
2.80	50

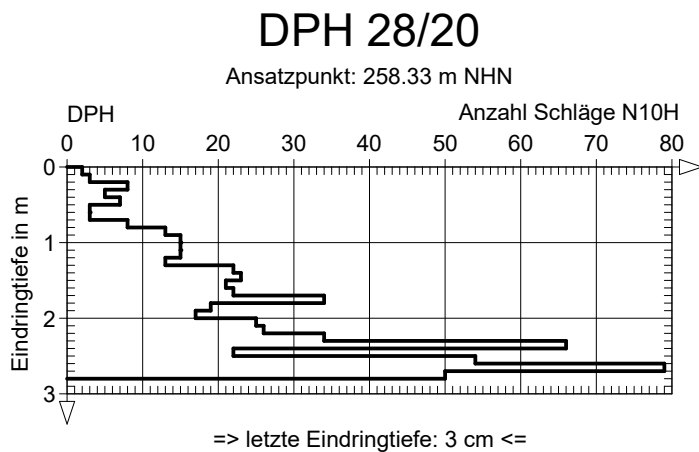


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 21.01.2021
89312 Günzburg-Deffingen	Koordinaten: 32536294.16 / 5678550.00	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	9
0.20	3
0.30	3
0.40	2
0.50	3
0.60	3
0.70	4
0.80	3
0.90	3
1.00	3
1.10	3
1.20	6
1.30	9
1.40	10
1.50	13
1.60	20
1.70	20
1.80	22
1.90	11
2.00	10
2.10	6
2.20	6
2.30	4
2.40	5
2.50	5
2.60	5
2.70	5
2.80	5
2.90	6
3.00	7
3.10	9
3.20	11
3.30	6
3.40	4
3.50	4
3.60	3
3.70	5
3.80	3
3.90	9
4.00	5
4.10	7
4.20	8
4.30	13
4.40	8
4.50	5
4.60	4
4.70	5
4.80	4
4.90	10
5.00	13
5.10	6
5.20	9
5.30	6
5.40	5
5.50	9
5.60	8
5.70	6

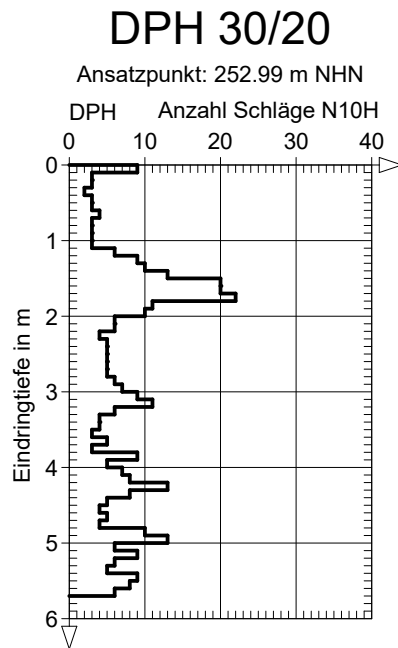


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 10.03.2021
89312 Günzburg-Deffingen	Koordinaten: 32536160.77 / 5678556.79	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaepmann

Tiefe	N ₁₀
0.10	1
0.20	1
0.30	1
0.40	1
0.50	1
0.60	1
0.70	2
0.80	4
0.90	7
1.00	8
1.10	11
1.20	10
1.30	10
1.40	10
1.50	9
1.60	10
1.70	11
1.80	13
1.90	73
2.00	19
2.10	12
2.20	14
2.30	20
2.40	11
2.50	21
2.60	18
2.70	15
2.80	51
2.90	100

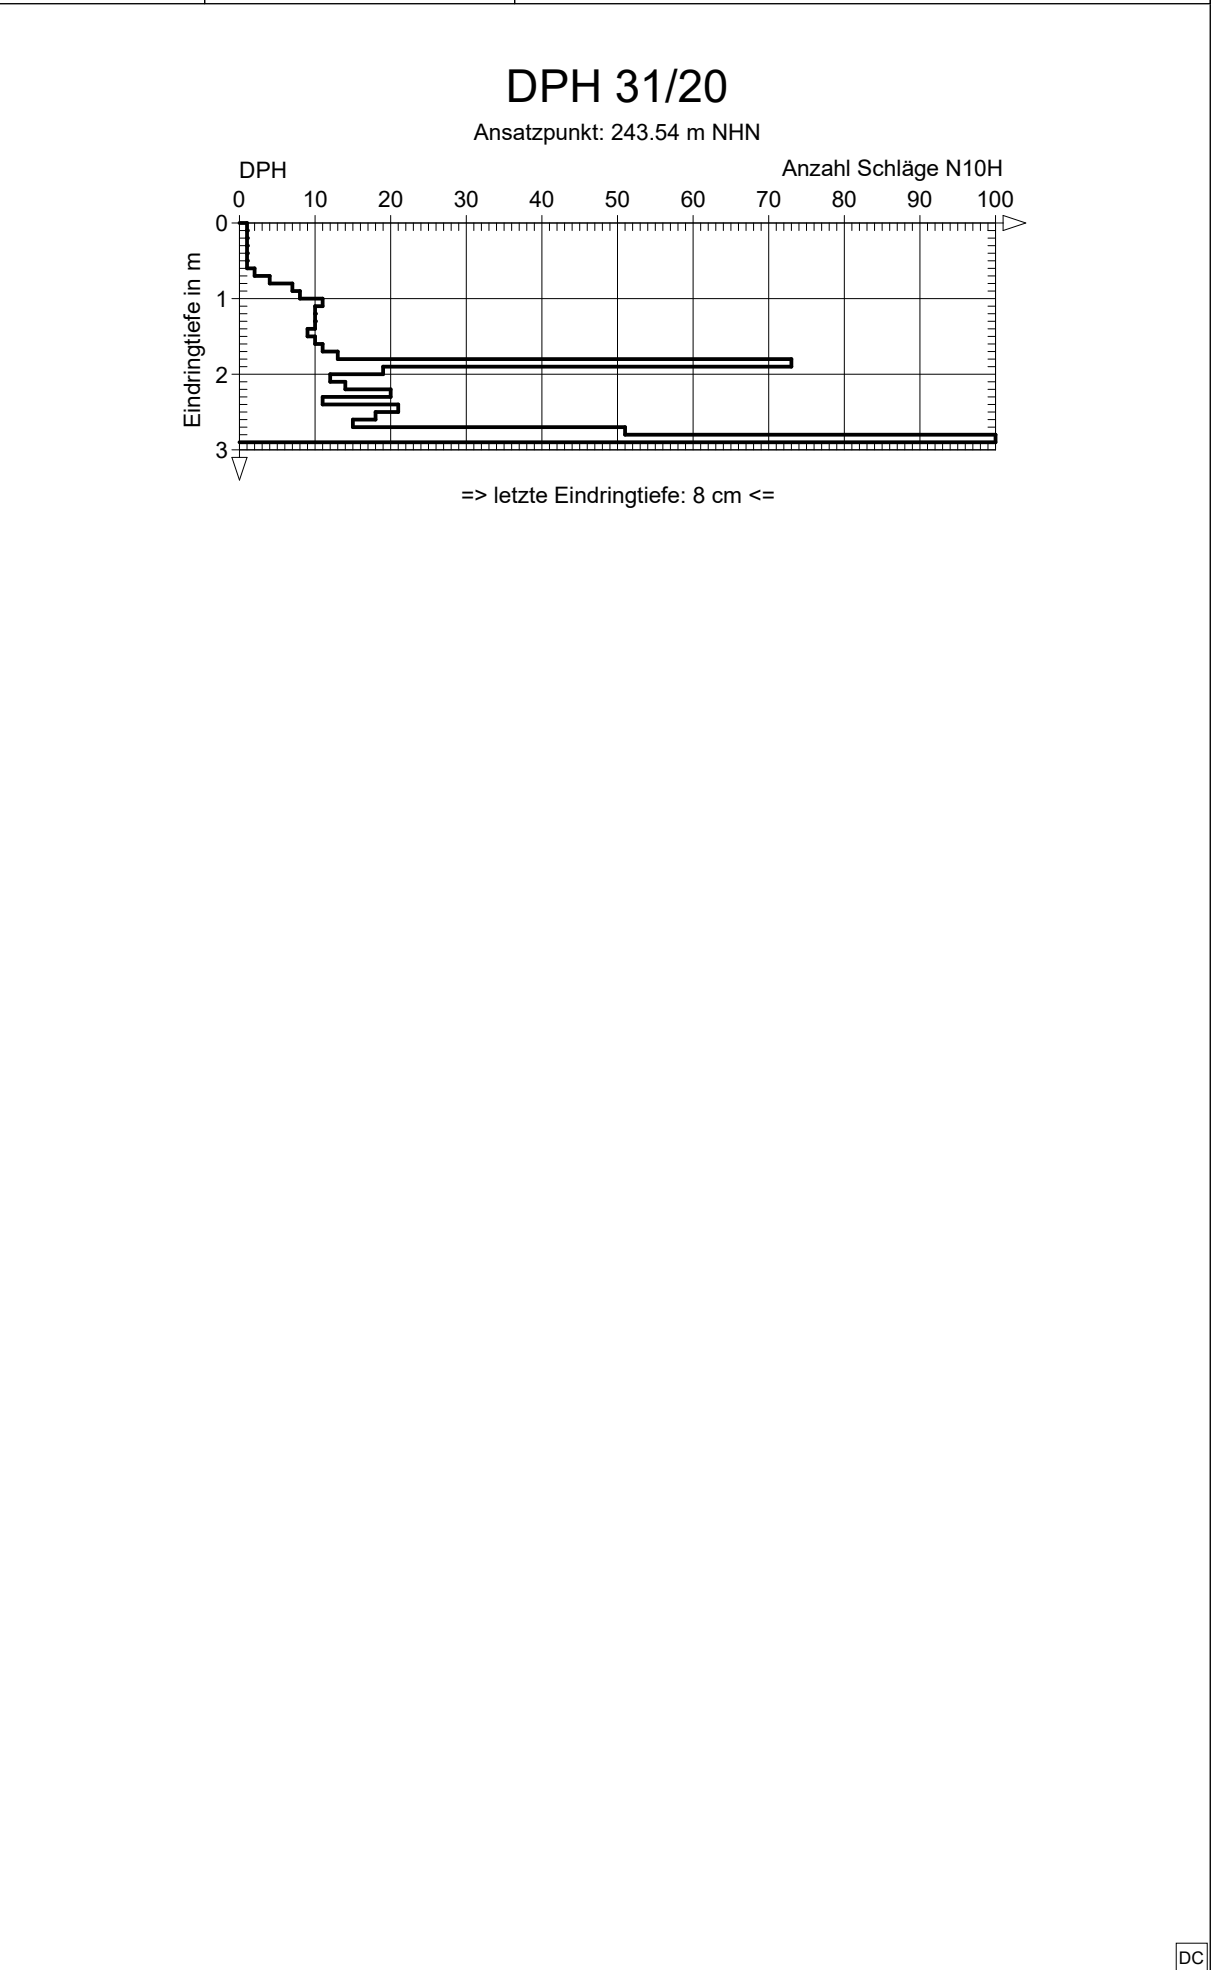

Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 10.03.2021
89312 Günzburg-Deffingen	Koordinaten: 32536150.58 / 5678639.24	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	2
0.20	2
0.30	2
0.40	2
0.50	6
0.60	6
0.70	6
0.80	4
0.90	3
1.00	2
1.10	3
1.20	2
1.30	2
1.40	3
1.50	3
1.60	2
1.70	3
1.80	3
1.90	2
2.00	2
2.10	2
2.20	2
2.30	2
2.40	2
2.50	3
2.60	3
2.70	3
2.80	4
2.90	7
3.00	7
3.10	7
3.20	6
3.30	9
3.40	7
3.50	11
3.60	7
3.70	9
3.80	11
3.90	9
4.00	11
4.10	11
4.20	9
4.30	18
4.40	14
4.50	10
4.60	11
4.70	8
4.80	12
4.90	14
5.00	12

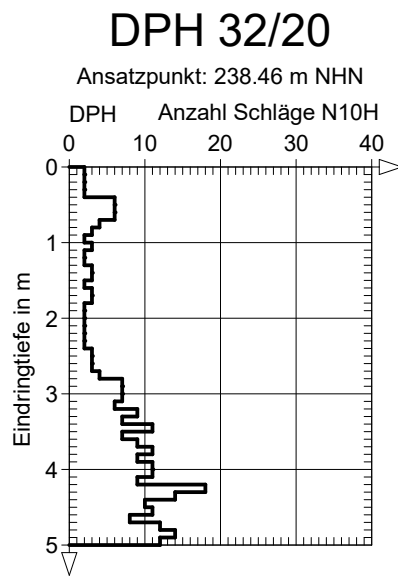


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 19.04.2021
89312 Günzburg-Deffingen	Koordinaten: 32536018.05 / 5678399.08	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	1
0.20	3
0.30	3
0.40	3
0.50	6
0.60	8
0.70	6
0.80	5
0.90	4
1.00	4
1.10	3
1.20	2
1.30	2
1.40	2
1.50	3
1.60	3
1.70	6
1.80	4
1.90	5
2.00	10
2.10	9
2.20	6
2.30	4
2.40	3
2.50	5
2.60	4
2.70	4
2.80	3
2.90	2
3.00	4
3.10	4
3.20	4
3.30	4
3.40	60
3.50	8
3.60	8
3.70	19
3.80	35
3.90	38
4.00	90
4.10	23
4.20	14
4.30	14
4.40	30
4.50	14
4.60	16
4.70	15
4.80	15
4.90	18
5.00	17

DPH 33/20

Ansatzpunkt: 247.96 m NHN

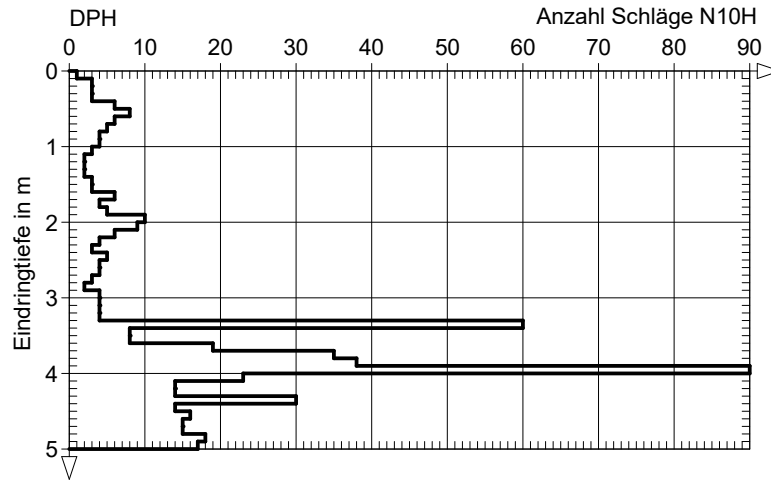


Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 19.04.2021
89312 Günzburg-Deffingen	Koordinaten: 32535952.30 / 5678350.01	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaeppmann

Tiefe	N ₁₀
0.10	1
0.20	2
0.30	3
0.40	4
0.50	3
0.60	5
0.70	5
0.80	3
0.90	1
1.00	1
1.10	1
1.20	3
1.30	3
1.40	3
1.50	3
1.60	3
1.70	6
1.80	6
1.90	6
2.00	6
2.10	15
2.20	16
2.30	10
2.40	14
2.50	9
2.60	7
2.70	9
2.80	9
2.90	6
3.00	5
3.10	6
3.20	8
3.30	6
3.40	6
3.50	8
3.60	5
3.70	5
3.80	3
3.90	3
4.00	5
4.10	5
4.20	11
4.30	19
4.40	10
4.50	10
4.60	7
4.70	5
4.80	11
4.90	51
5.00	32

DPH 34/20

Ansatzpunkt: 247.26 m NHN

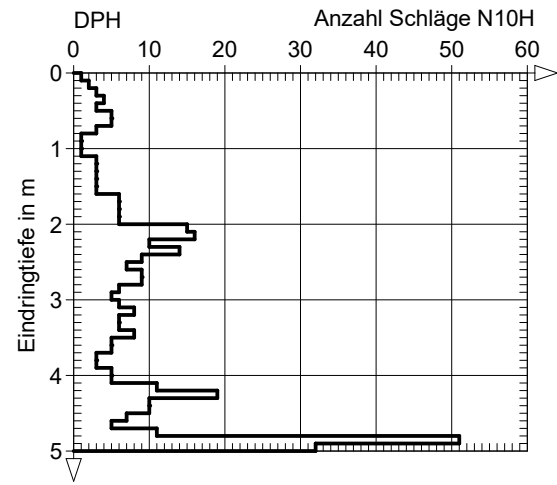

Terrasond GmbH & Co.KG	Projekt: AK Kassel-W - AD Kassel-S Berghäuser Brücke	
St.-Ulrich-Straße 12-16	Projektnr.: 2020-1029	Datum: 25.02.2021
89312 Günzburg-Deffingen	Koordinaten: 32536075.02 / 5678081.35	
Tel.: 08221/906-0/ Fax: -40	Maßstab: 1: 100	Ausgeführt von: Andreas Schaepmann

Tiefe	N ₁₀
0.10	1
0.20	6
0.30	6
0.40	2
0.50	1
0.60	1
0.70	1
0.80	1
0.90	1
1.00	1
1.10	3
1.20	2
1.30	3
1.40	2
1.50	2
1.60	2
1.70	3
1.80	5
1.90	5
2.00	4
2.10	5
2.20	5
2.30	5
2.40	6
2.50	8
2.60	8
2.70	7
2.80	22
2.90	15
3.00	6
3.10	11
3.20	9
3.30	6
3.40	12
3.50	24
3.60	22
3.70	30
3.80	16
3.90	22
4.00	16
4.10	15
4.20	15
4.30	14
4.40	14
4.50	17
4.60	23
4.70	24
4.80	40
4.90	28
5.00	42

